Name: Yash Singh	Subject: Agile Software Development & DevOps
T.E. Batch: T22 Sem: 5th Roll No: 2401118	Date: 17/10/26

EXPERIMENT

Jira Agile Project Management using Scrum (CampusConnect)

Name:	Yash Singh	**Roll No.:**	2401118
Project:	CampusConnect	**Methodology:**	Scrum

1. Aim

To set up and manage an Agile Scrum project in Jira for the CampusConnect project, covering epics, work items, sprint planning, issue dependencies, the sprint board and project reporting.

2. Objective

- To create a Scrum project in Jira and invite the team members.
- To create epics and break them into work items in the backlog.
- To plan Sprint 1 with a sprint goal and link dependent work items.
- To track work progress on the sprint board and review it using the Timeline and Summary views.

3. Software / Tools Required

- Jira Software (web version, Free plan) with the Scrum template
- Web browser with an internet connection

4. Brief Theory / Concept

Scrum is an Agile framework in which work is delivered in short time-boxed iterations called sprints. In Jira, work is organised in the following hierarchy:

Level	Description
Roadmap	Top-level strategic goals of the project.
Epic	A large initiative broken into deliverables; managed by the Product Owner.
User Story	A functional requirement that delivers value to the user.
Task / Sub-task	Specific technical work completed by developers.

The Backlog holds all planned work items. Items selected for a sprint are moved into the sprint, and starting the sprint opens the Active Board where progress is tracked.

5. Procedure / Step-by-Step Implementation

1. Open the Jira website and select "Get Jira for free".
2. Register using a work email, verify with the security code, enter the full name, create a password and enter the organization domain.
3. Select "Software Development" as the work type and choose the "Scrum" methodology.
4. Create the project named "CampusConnect".
5. Click the team icon in the top navigation bar, enter the email addresses of the collaborators and click "Add people".
6. Create the epics, then create work items in the Backlog and assign each to its parent epic and a team member.
7. Link the dependent work items using the "is blocked by" relationship.
8. Edit Sprint 1 (dates and sprint goal), move the work items into it and click "Start sprint".
9. Add a custom "Review" column on the board between "In Progress" and "Done".
10. Use the Timeline and Summary views to monitor and report the progress.

6. Jira Project Configuration

Setting	Value
Project name	CampusConnect
Issue key prefix	CC
Work type / Methodology	Software Development / Scrum
Navigation tabs	Summary, Backlog, Board, Calendar, Timeline, Docs, Forms

Team members added to the project:

Sr.	Team Member	Initials shown in Jira
1	Pratham Tapadia	P
2	Yash Singh	AV
3	Komal Yannam	K

The project home page (Summary view) with the team and its workload is shown in Figure 1.

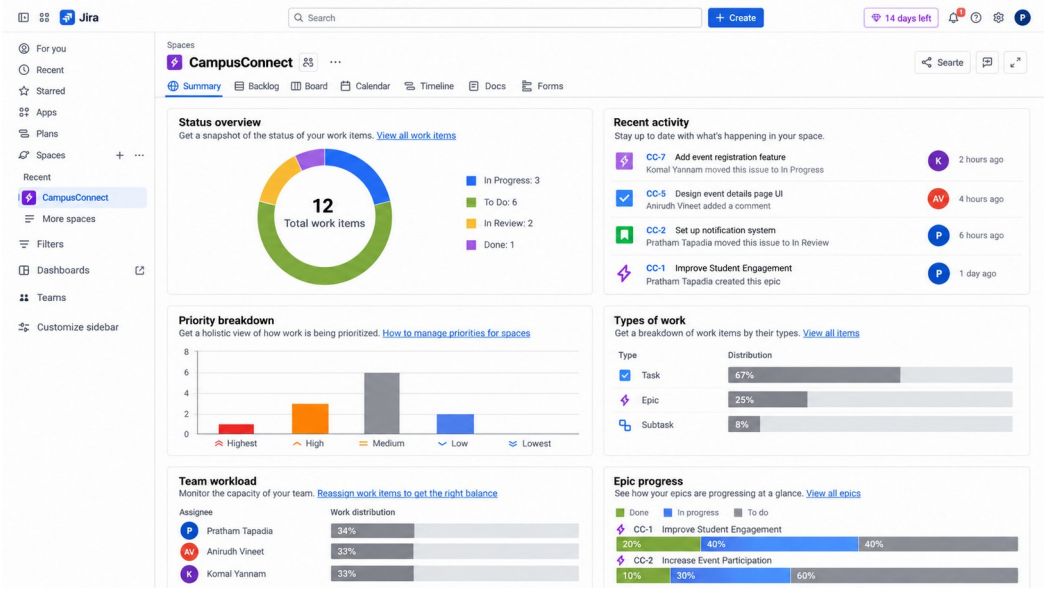


Figure 1: CampusConnect Jira Project Summary

7. Epics and Work Items

Two epics were configured for CampusConnect:

Epic	Purpose
Improve Student Engagement	Features that keep students informed and engaged with campus activities.
Increase Event Participation	Features that encourage students to take part in campus events.

Work items created in the Backlog and linked to their parent epics:

Key	Type	Summary	Parent Epic	Assignee
CC-1	Story	Provide live campus event updates	Improve Student Engagement	Pratham Tapadia
CC-2	Story	Add WhatsApp notifications	Improve Student Engagement	Yash Singh
CC-3	Story	Add email notifications	Improve Student Engagement	Komal Yannam
CC-4	Story	Create a campus resource knowledge base	Improve Student Engagement	Pratham Tapadia

Key	Type	Summary	Parent Epic	Assignee
CC-5	Story	Create a review system for campus events	Increase Event Participation	Yash Singh

All work items were given Medium priority.

8. Sprint Planning

1. Open the context menu of Sprint 1 and select "Edit sprint".
2. Set the sprint duration from 3 June to 1 July.
3. Enter the sprint goal: "Improving student experience on our campus platform".
4. Move CC-1, CC-2 and CC-3 from the Backlog into Sprint 1.
5. Keep CC-4 and CC-5 in the Backlog for later sprints.

Sprint 1 Detail	Value
Duration	3 June – 1 July
Sprint goal	Improving student experience on our campus platform
Work items in sprint	CC-1, CC-2, CC-3 (3 work items)
Work items in backlog	CC-4, CC-5 (2 work items)

The Backlog view with Sprint 1 and the remaining backlog is shown in Figure 2.

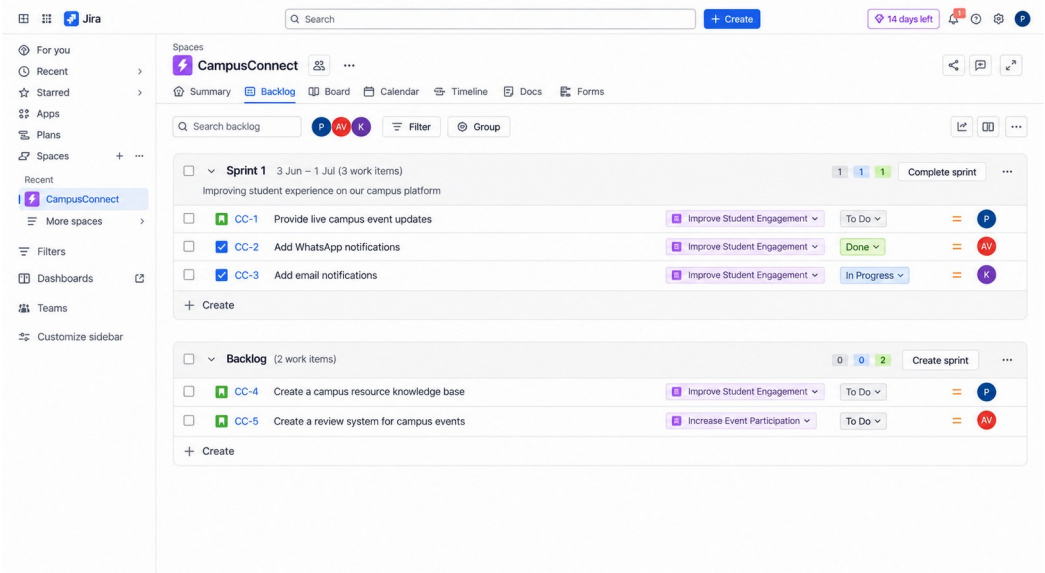


Figure 2: CampusConnect Sprint Backlog

9. Issue Dependencies

To deliver the story CC-1 (Provide live campus event updates), the notification work items must be completed first. CC-1 was linked to CC-2 and CC-3 using the relationship "is blocked by".

Work Item	Summary	Relationship	Blocked By
CC-1	Provide live campus event updates	is blocked by	CC-2 (Add WhatsApp notifications), CC-3 (Add email notifications)

10. Sprint Board / Workflow

Clicking "Start sprint" moves Sprint 1 to the Active Board. Each work item appears as a card showing its parent epic, key, priority and assignee. Cards are moved across columns as work progresses:

Status	Meaning
To Do	Work item is planned but not started.

Status	Meaning
In Progress	Work item is being developed by the assignee.
Review	Custom column added between In Progress and Done for reviewing completed work.
Done	Work item is completed.

In the Backlog (Figure 2), CC-2 is Done, CC-3 is In Progress and CC-1 is still To Do. The Active Board is shown in Figure 3.

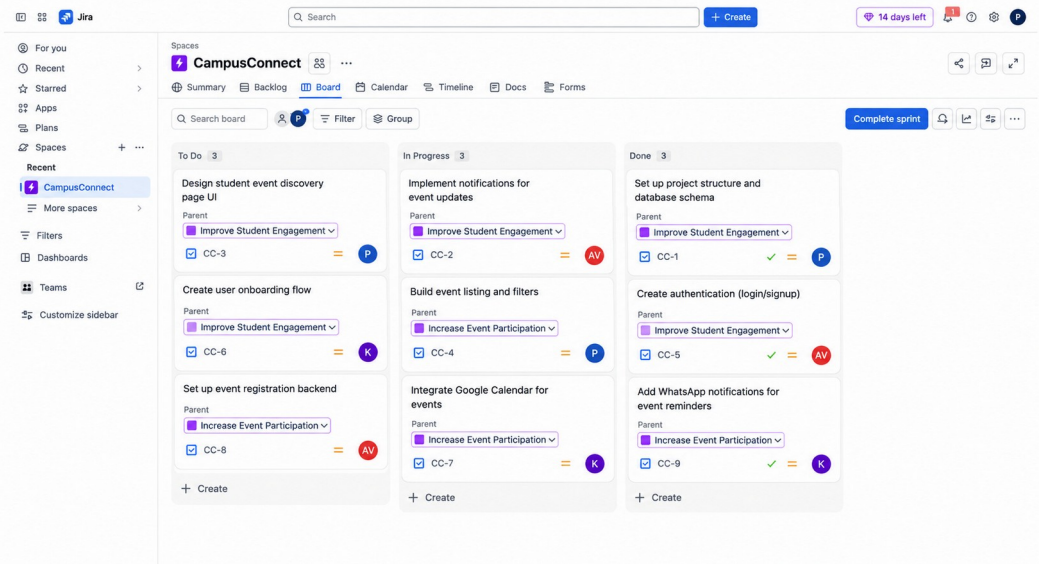


Figure 3: CampusConnect Active Sprint Board

11. Timeline / Reporting

- Timeline (Gantt) view: shows the epics and their child work items across the sprint dates, along with dependency arrows between linked items.
- Summary view (Figure 1): gives a project overview through Status overview, Recent activity, Priority breakdown, Types of work, Team workload and Epic progress.
- Team workload in the Summary view shows the work divided almost equally among Pratham Tapadia, Anirudh Vineet and Komal Yannam.

12. Screenshots / Results

Figure	Jira View	Shows
Figure 1	Summary	Project overview, team workload and epic progress
Figure 2	Backlog	Sprint 1 with its goal and dates, work items, parent epics and the remaining backlog
Figure 3	Board	Active sprint board with work items in their status columns

13. Conclusion

A Scrum project named CampusConnect was set up in Jira with three team members. Two epics and five work items were created, Sprint 1 was planned with a sprint goal and dependent items were linked. Progress was tracked on the Active Board and reviewed using the Summary and Timeline views, which demonstrated how Jira supports Agile project management.
